Hawkeye Pedershaab
Concrete Technologies Worldwide ™

M CON
PIPE & PRODUCTS INC

2691 Greenfield Road
Ayr, ON N0B 1E0 Canada

# Smartcast Basesection Designer. Order/Offer

| | |
|---|---|
| Customer | NASIO GROUP INC |
| Delivery address | |
| Project No. | TMU RESEARCH AREA |
| | |
| | |
| EPS Ø x H | 1220 / 483 |

| | |
|---|---|
| Order no. | 251626_SANMH03_A |
| Date. | 07-01-2026 |
| Order Date | 07-01-2026 |
| Made by | mcon@mcon.com |

| | |
|---|---|
| Mould | 1220x127x762 2,5' |
| Basesection | 1220x127x762 2,5' |
| Height mm | 870 |
| Bottom inserts mm | 152 |
| Benching Height mm | 147 |
| Benching Slope 0/00 | 125 |
| Weight kg | 2196 kg |

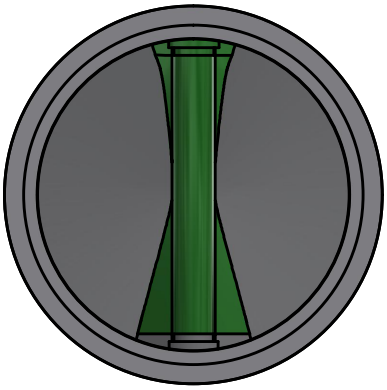

| | Main Inlet > | 1 | | | | |
|---|---|---|---|---|---|---|
| Outlet/Inlet | Outlet | Inlet 1 | Inlet 2 | Inlet 3 | Inlet 4 | Inlet 5 |
| Connections type | 150-6" PVC SDR 28 | 150-6" PVC SDR 28 | | | | |
| Gasket type | 10-06 PSX | 10-06 PSX | | | | |
| Dimension mm. | 150 | 150 | | | | |
| Angle 360° | 0 | 180 | | | | |
| Invert Level mm. | 0 | 60 | | | | |
| 2. Invert Level mm. | | 60 | | | | |
| Socket angle 0/00 | | | | | | |
| Channel Drop mm | | 60 | | | | |
| Straight section mm | | 50 | | | | |
| Note | | | | | | |

| | |
|---|---|
| Approved by. | |
| | |
| Control | |
| | |
| Date | |
| | |

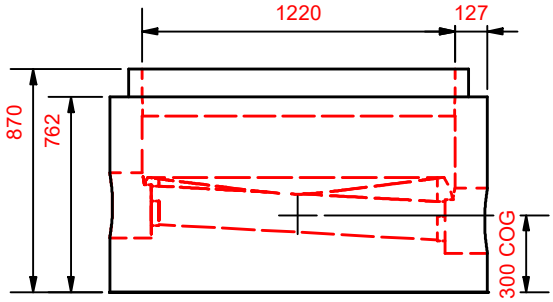


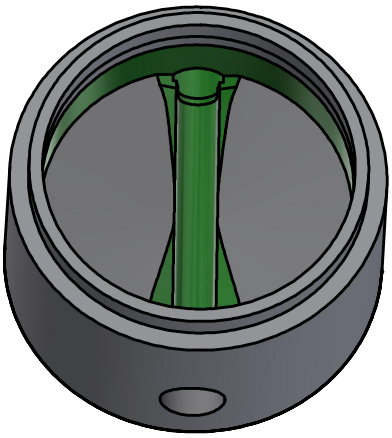

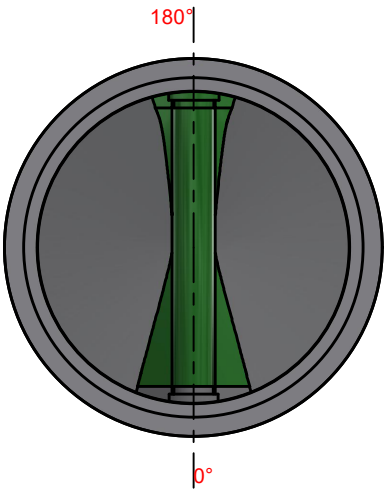

Hawkeye Pedershaab
Concrete Technologies Worldwide ™

M CON
PIPE & PRODUCTS INC

2691 Greenfield Road
Ayr, ON N0B 1E0 Canada

## Smartcast Basesection Designer.

| | |
|---|---|
| Customer | **NASIO GROUP INC** |
| Delivery address | |
| Project No. | **TMU RESEARCH AREA** |
| | |
| | |
| Basesection | **1220x127x762 2,5'** |
| Order no. | **251626_SANMH03_A** |
| Order Date | **07-01-2026** |
| Weight kg | **2196 kg** |

| | |
|---|---|
| Center of gravity | 300 |
| EPS raw height | 483 |
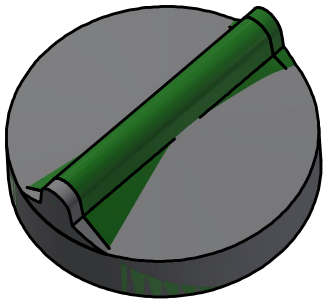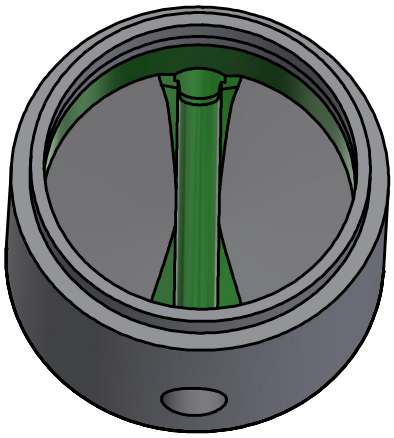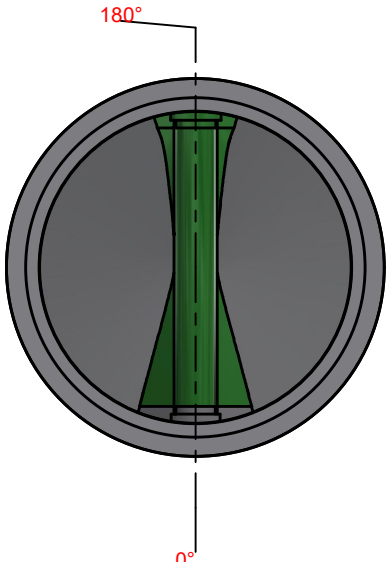
| | Main Inlet > | 1 | | | | |
|---|---|---|---|---|---|---|
| Outlet/Inlet | Outlet | Inlet 1 | Inlet 2 | Inlet 3 | Inlet 4 | Inlet 5 |
| Angle 360° | 0 | 180 | | | | |
| Invert Level mm. | 0 | 60 | | | | |
| Connections type | 150-6" PVC SDR 28 | 150-6" PVC SDR 28 | | | | |
