Hawkeye Pedershaab
Concrete Technologies Worldwide ™

M CON
PIPE & PRODUCTS INC

2691 Greenfield Road
Ayr, ON N0B 1E0 Canada

Smartcast Basesection Designer. Order/Offer

Customer	TRISAN CONSTRUCTION
Delivery address	BASEMENT FLOODING PROTECTION PROGRAM PHASE 4 ASSIGNMENTS 41-03 & 41-06
Project No.	
EPS Ø x H	1220 / 1094

Order no.	25694_BR06_A
Date.	17-11-2025
Order Date	17-11-2025
Made by	mcon@mcon.com

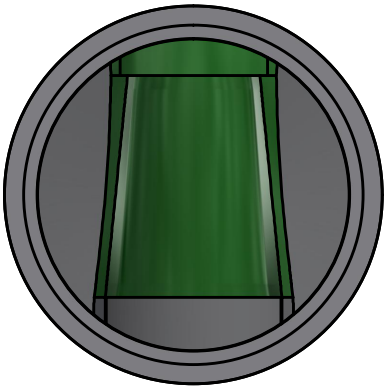

Mould	1220x127x1448 4,75'
Basesection	1220x127x1448 4,75'
Height mm	1556
Bottom inserts mm	152
Benching Height mm	610
Benching Slope 0/00	125
Weight kg	3487 kg

	Main Inlet >	1				
Outlet/Inlet	Outlet	Inlet 1	Inlet 2	Inlet 3	Inlet 4	Inlet 5
Connections type	600-24" Concrete	450-18" Concrete				
Gasket type	S306-34L	28A PSX-2				
Dimension mm.	610	457				
Angle 360°	0	180				
Invert Level mm.	0	220				
2. Invert Level mm.		150				
Socket angle 0/00						
Channel Drop mm		150				
Straight section mm		50				
Note						

Approved by.	
Control	
Date	

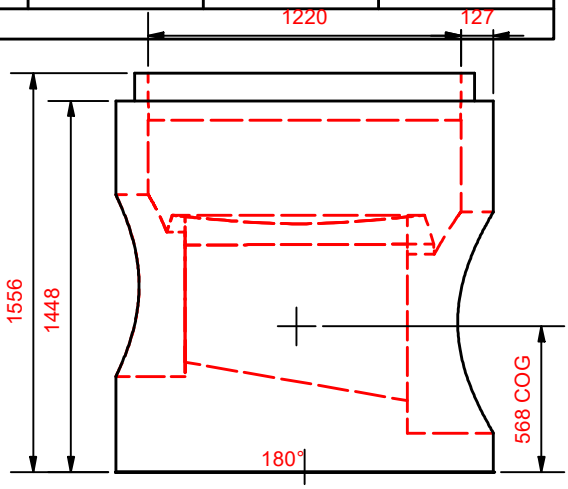

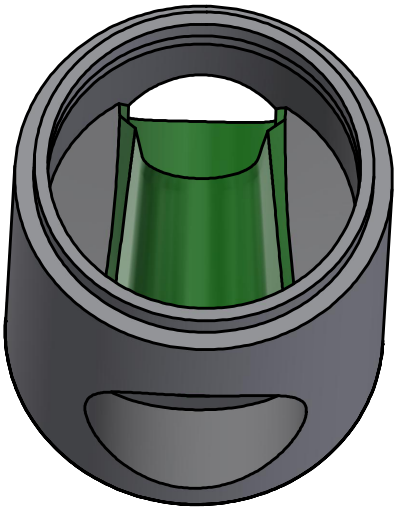

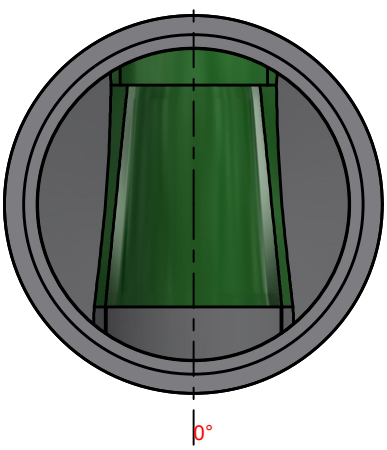

Hawkeye Pedershaab
Concrete Technologies Worldwide ™

M CON
PIPE & PRODUCTS INC

2691 Greenfield Road
Ayr, ON N0B 1E0 Canada

Smartcast Basesection Designer.

Customer	TRISAN CONSTRUCTION
Delivery address	BASEMENT FLOODING PROTECTION PROGRAM PHASE 4 ASSIGNMENTS
Project No.	41-03 & 41-06
Basesection	1220x127x1448 4,75'
Order no.	25694_BR06_A
Order Date	17-11-2025
Weight kg	3487 kg

Center of gravity	568
EPS raw height	1094
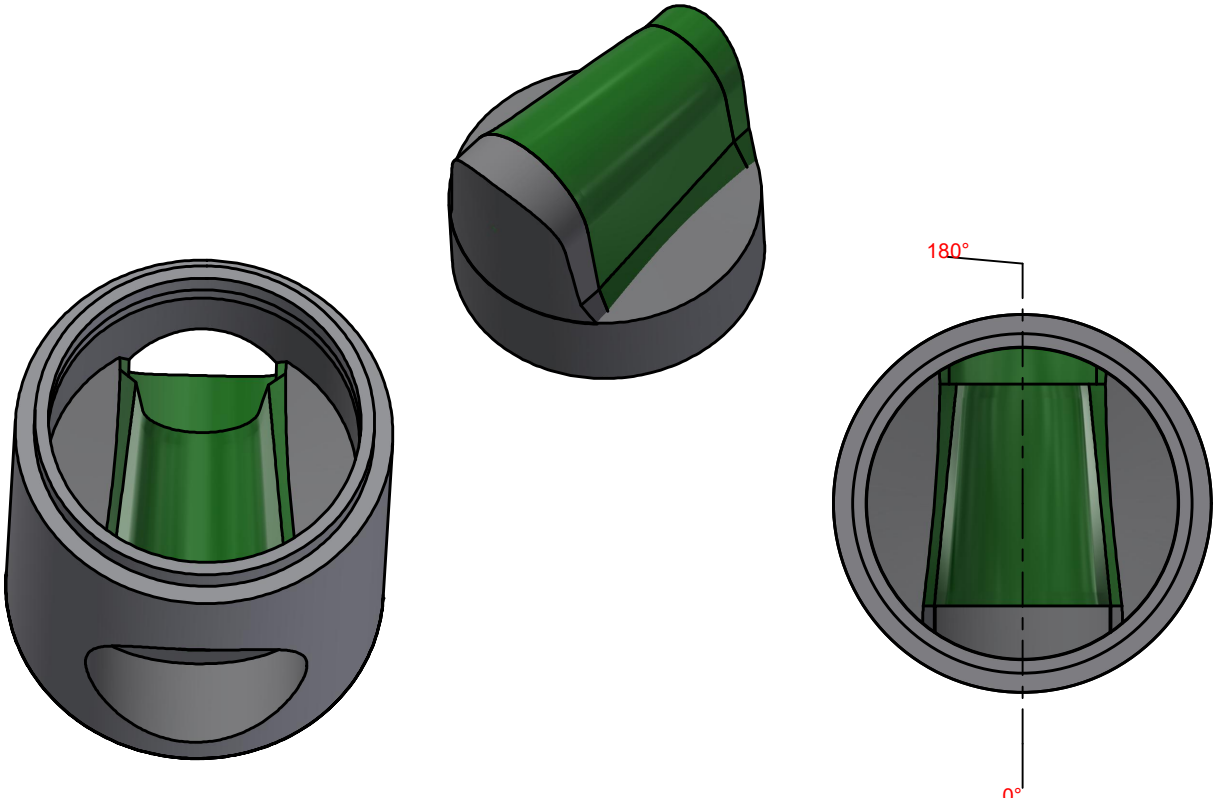
	Main Inlet >	1				
Outlet/Inlet	Outlet	Inlet 1	Inlet 2	Inlet 3	Inlet 4	Inlet 5
Angle 360°	0	180				
Invert Level mm.	0	220				
Connections type	600-24" Concrete	450-18" Concrete
