Hawkeye Pedershaab
Concrete Technologies Worldwide ™

M CON
PIPE & PRODUCTS INC

2691 Greenfield Road
Ayr, ON N0B 1E0 Canada

Smartcast Basesection Designer. Order/Offer

Customer	J-AAR EXCAVATING LIMITED
Delivery address	PROPOSED RESIDENTIAL BUILDING TOWER A 15 CAPULET WALK
Project No.	
EPS Ø x H	1220 559

Order no.	25990_SANMH03_A
Date.	22-01-2026
Order Date	22-01-2026
Made by	mcon@mcon.com

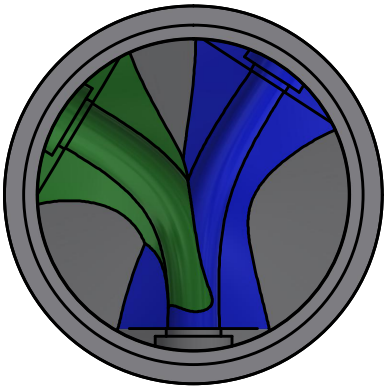

Mould	1220x127x838 2,75'
Basesection	1220x127x838 2,75'
Height mm	946
Bottom inserts mm	152
Benching Height mm	101
Benching Slope 0/00	125
Weight kg	2082 kg

	Main Inlet >		1			
Outlet/Inlet	Outlet	Inlet 1	Inlet 2	Inlet 3	Inlet 4	Inlet 5
Connections type	200-8" PVC SDR 35	200-8" PVC SDR 35	150-6" PVC SDR 28			
Gasket type	12-08 PSX	12-08 PSX	10-06 PSX			
Dimension mm.	201	201	150			
Angle 360°	0	121	213			
Invert Level mm.	0	30	60			
2. Invert Level mm.		30	60			
Socket angle 0/00						
Channel Drop mm		30	60			
Straight section mm		50	50			
Note						

Approved by.	
Control	
Date	

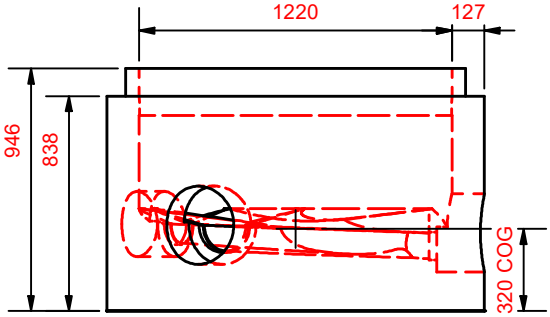

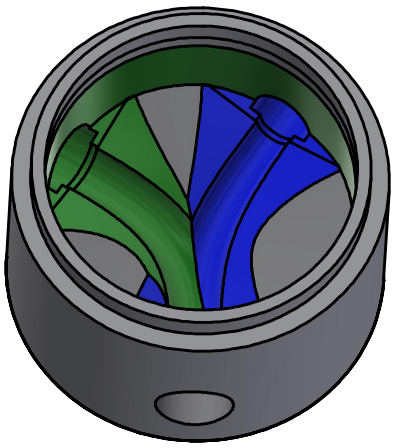

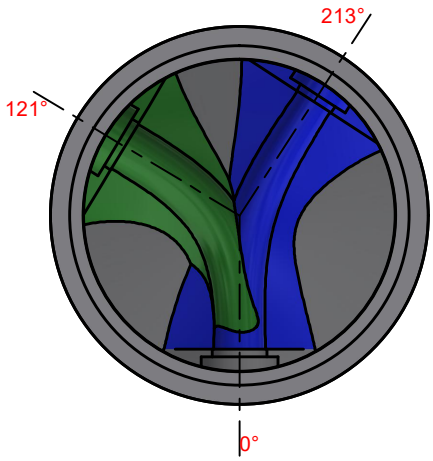

Hawkeye Pedershaab
Concrete Technologies Worldwide ™

M CON
PIPE & PRODUCTS INC

2691 Greenfield Road
Ayr, ON N0B 1E0 Canada

Smartcast Basesection Designer.

Customer	J-AAR EXCAVATING LIMITED
Delivery address	PROPOSED RESIDENTIAL
Project No.	BUILDING TOWER A 15
	CAPULET WALK
Basesection	1220x127x838 2,75'
Order no.	25990_SANMH03_A
Order Date	22-01-2026
Weight kg	2082 kg

Center of gravity	320
EPS raw height	559
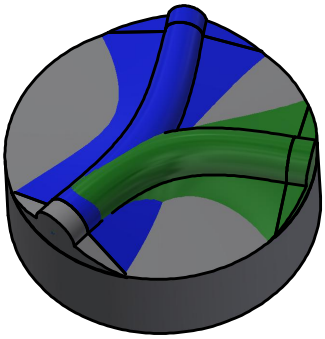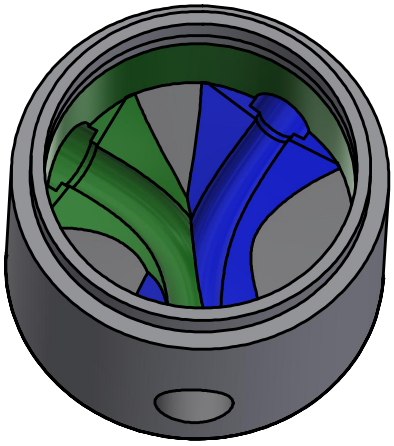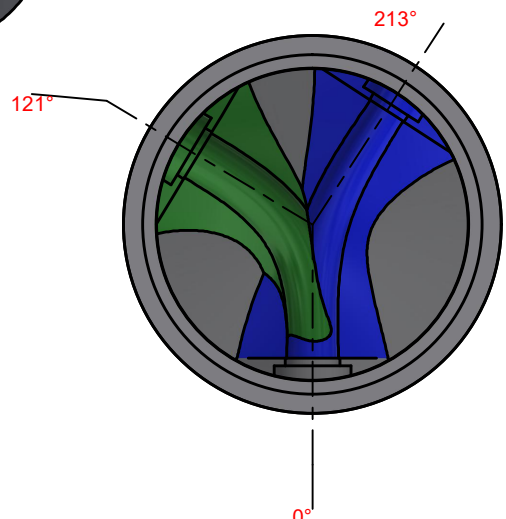
	Main Inlet >		1			
Outlet/Inlet	Outlet	Inlet 1	Inlet 2	Inlet 3	Inlet 4	Inlet 5
Angle 360°	0	121	213			
Invert Level mm.	0	30	60			
Connections type	200-8" PVC SDR 35	200-8" PVC SDR 35	150-6" PVC SDR 28
